

TUBBS FIRE RECOVERY PROJECTS UPDATE




Cat	FEMA Project #	EMMIE PW #	CIP Project #	Project Name	Status	% Complete	Ant. Completion Date
Α	38594	323		Vegetative debris within Fountaingrove and Coffey Park neighborhoods	Complete	100%	
Α	64204	353		Hazard Tree Removal	Construction	70%	Winter 2021
В	38591	324		Citywide Emergency Protective Procedures First 30 days	Complete	100%	
В	38592	328		Emergency Protective Procedures-Citywide-Remaining Period 31 Days Plus	Complete	100%	
В	38593	259		TPW Emergency Protective Measures. First 30 days	Complete	100%	
В	38852	280		Water Dept. Emerg. Protc. Measures First 30 days	Complete	100%	
В	40509	315		Water Dept. Emerg. Protc. Measures First 31 days	Complete	100%	
В	40510	275		TPW 31 Plus Emerg. Protective Measures	Complete	100%	
В	102107	352		City of Santa Rosa Sewer Lateral Plugging	Complete	100%	
С	36351	124	2226, 2233	Roads,signs,poles,& melted conduit City Wide	Complete	100%	
С	36353	120	2247	Roads & Bridges-Vehicular Bridges	Pending	0%	Fall 2021
С	36383	293	2227	Road & Bridges-Storm Drain, Pipes, Catch Basins, & Drop Inlets	Pending	0%	Fall 2021
С	37170	312	2176, 2178, 2179	City wide work completed storm drains	Complete	100%	
С	37829	221	2245	Roads & Bridges City-wide asphalt & pavement damage from Burnt Debris	Pending	0%	Fall 2021
E	36366	147	2184	Bldg. & Equip. Fire St. 5 Bldg.	Scoping	5%	Fall 2024
E	36370	291	2183	Bldg. & Equip. Former Fire St. 5 Bldg	Complete	100%	
E	36371	119	-	Bldg. & Equip. Vehicle Losses & Sign Damage	Complete	100%	
E	42404	192	2183	Temp. Relocation of New Fire St. 5	Complete	100%	
F	36373	229	2208	Utilities-Portable Water Pumps & Reservoirs	Construction	75%	Fall 2021
F	36375	228	2208	Utilities-Sewer Lift Stations	Construction	75%	Fall 2021
F	36378	325	2222, 2213	Contaminated Water Supply System	Complete	100%	
F	37303	170	2208	Sewer Lift Station 1	Construction	75%	Fall 2021
F	38687	258	2240	Water Dept. Metering-City Wide-Water meter replacement	Complete	100%	
F	38691	187	2201	Sewer Lift Station - 2	Construction	25%	Winter 2021
F	38692	226	2201	Sewer Lift Station 20	Construction	25%	Winter 2021
G	36360	167	2249	Burned Parks Irrigation System	Design	50%	Fall 2022
G	36379	173	2229	Pedestrian Bridge at Francis Nielsen Park, Parker Hill Road	Complete	100%	
G	36380	193	2248	Parks, Fences, Recreation & Other City Wide	Design	50%	Fall 2022
Z	39364	359		City of Santa Rosa PAAP-DAC	Pending		

Page 7

GENERAL FUND PROJECTS SUMMARY



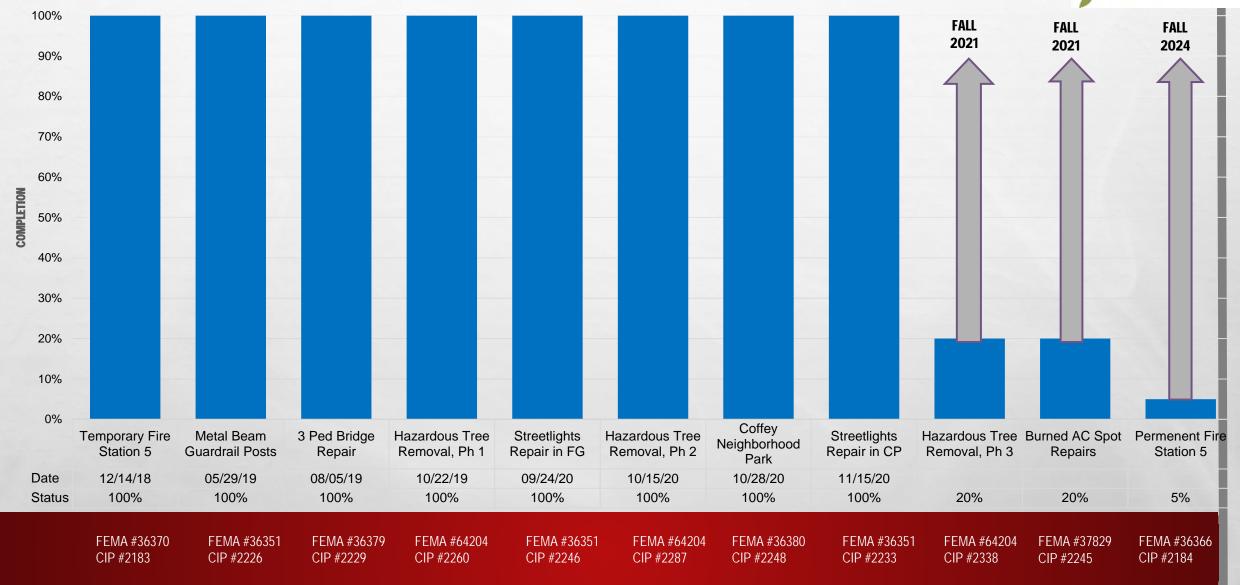

GENERAL FUND PROJECT SUMMARY (CONT.)

- CROSS CREEK VEHICLE BRIDGE FENCE REPAIR - 0% COMPLETE
 - FEMA #36353
 - CIP #2247
- FIRE DAMAGED STORM DRAIN REPAIRS 0% COMPLETE (18 DROP INLET LIDS)
 - FEMA #36383
 - CIP #2227
- VEHICLE LOSSES AND SIGN DAMAGE - 100% COMPLETE
 - FEMA #36371

- BURNED PARK OPEN SPACE
 IRRIGATION 50% COMPLETE
 - FEMA #36360
 - CIP #2249
- COFFEY NEIGHBORHOOD PARK & DAMAGE AT 6 PARKS - 50%
 COMPLETE
 - FEMA #36380
 - CIP #2248



FEMA PROJECT NO. 42409 - Temporary Fire Station 5

Total Construction Cost: \$1.2M



The former Fire Station 5 on Parker Hill Road was selected as the site







Completed December 2018

FEMA PROJECT NO. 36351 - ROADS, SIGNS, MELTED CONDUITS

Construction Cost: \$ 2,286,241





101 Metal beam burned guardrail posts replaced



228 streetlights restored in Coffey Park including

- · 2.5 miles of new conduits
- 128 new streetlight poles & foundations
- 100 new light fixtures



41 Streetlights restored in Fountaingrove



FEMA PROJECT NO. 36379 - PEDSTRAIN BRIDGES

Construction Cost: \$ 90,758













Wood bridge at Francis Nielsen Park

 Fire retardant deck with added structural support using existing abutments







FEMA PROJECT NO. 36380 & 36360 - PARKS & IRRIGATIONS

Construction Cost: \$ 3,209,981

COFFEY NEIGHBORHOOD PARK















FEMA PROJECT NO. 64204 - HAZARDOUS TREE REMOVAL Estimated Construction Cost: \$ 350,000

Phase 1 - 450 Street trees removed

Phase 2 - 133 Trees in medians, open space, and parks removed

Phase 3 - Still in design, but approx. 100 trees within the open space and parks will be removed by the end of 2021







IN-PROGRESS GENERAL FUND PROJECT

FEMA PROJECT NO. 36360 & 36380 - Six Fire Damaged Parks

Construction Cost: \$ 2,439,866 **Status:** 100% **Design Complete**

Expected Completion: Spring 2022

- Rincon Ridge Open Space
- Rincon Ridge Neighborhood Park
- Fir Ridge Neighborhood Park
- Nagasawa Community Park
- Francis Nielsen Neighborhood Park
- Parkerhill Trail















IN-PROGRESS GENERAL FUND PROJECT

HMGP PROJECT NO. PJ0351 - Roadway Landscape Recovery

FEMA PROJECT NO. 36360 & 36380

Construction Cost: \$ 9,017,185 Status: 100% design complete

Expected Completion: Summer 2022

 The HMGP has been combined with the FEMA project as a cost effective delivery solution












WATER ENTERPRISE PROJECT SUMMARY Santa Rosa

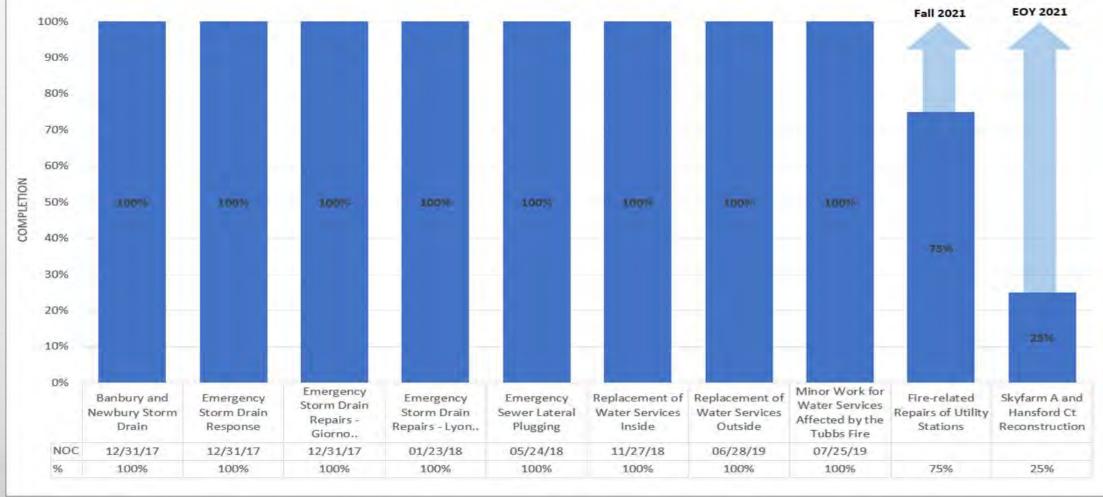

FEMA #37170 CIP #2176 CIP #2178 CIP #2179 FEMA #36378 FI

FEMA #36378 CIP #2213 FEMA #38687 CIP #2240 FEMA #36373 FEMA #36375 FEMA #37303

CIP #2208

FEMA #38691 FEMA #38692 CIP #2201

IN-PROCESS ENTERPRISE FUND PROJECTS

FEMA PROJECT NO. 38687- Water Meter Replacement Project

Construction Cost: \$ 1,900,000

 Meters, endpoints and meter boxes were damaged by extreme heat

 While substantially complete, official completion date will come with final meter sets for all rebuilt properties





IN-PROGRESS ENTERPRISE FUND PROJECTS

FEMA PROJECT NOs. 38691 & 38692 - Skyfarm 'A' & Hansford Ct Lift Stations

Construction Cost: \$ 3,400,000


Estimated Completion: Winter 2021

- Hansford Ct bypass manhole and temp power installed
- Hansford Ct finishing concrete work and equipment pad installation
- Skyfarm A potholing and coordinating with PG&E for temp power - met on site 1/12/21
- Skyfarm A demolition work begins March 1












IN-PROGRESS ENTERPRISE FUND PROJECTS

FEMA PROJECT NOs. 36373, 36375 & 37303 - Fire Related Repairs of Utility Stations

Construction Cost: \$ 1,400,000 Estimated Completion: Fall 2021

- Repairs 14 Water Dept. Facilities
- Fencing and Gates complete all sites
- Site work ongoing at Sewer Lift Station 1



- Remaining work at various sites:
 - Antenna at Water Station 1
 - Generator Enclosure at Sewer Lift Station 5
 - Site work at Well 6



COMPLETED ENTERPRISE FUND PROJECTS

- WATER CONTAMINATION PROJECT
 - 100% COMPLETE
 - FEMA #36378
 - CIP #2222 & 2213
 - CONSTRUCTION COST: \$8,400,000
 - CLOSEOUT AND REIMBURSEMENT SUBMITTED
- SEWER LATERAL PLUGGING
 - 100% COMPLETE
 - FEMA #102107
 - CIP #2227
 - CONSTRUCTION COST: \$148,000
 - CLOSEOUT SUBMITTED

