

Staff Briefing: 2017 Tubbs Fire Recovery Projects Update

Joe Schiavone

Acting Director, Transportation and Public Works

Alan Alton,

Chief Financial Officer, Finance

Grant Bailey

Acting Deputy Director, Engineering Services

August 23, 2022



Fire Recovery Project Statistics

- 20 of 29 FEMA Public Assistance projects are complete
 - 4 completed since February 2022
 - 1 of 3 FEMA Hazard Mitigation Grant projects are complete
- 8 projects in final closeout
- 2 projects in construction
 - Six Fire Damaged Parks
 - Fire Damaged Roadway Landscaping
- Fire Station No. 5 Design Build Entity under contract Jan 2023
- Reimbursements to date = \$17.8 million

Completed Projects

Utilities (FEMA Obligated Amount: \$14.2M)

- Sewer Lift Stations:
 - Skyfarm
 - Hansford
 - Stagecoach
- Contaminated Water Supply System
- Storm Drain System Repairs

Infrastructure (FEMA Obligated Amount: \$18.3M)

- Signs, Poles & Electrical Conduit Replacement
- Coffey Neighborhood Park
- Pedestrian Bridges
- Battery Backup Retrofit



Projects in Design/Construction

7 Pending Projects

Design


1. Rebuild Fire Station 5 - CDBG
2. Fire Damaged Roadway Resiliency Improvement - CDBG
3. Arterial and Collector Roadway Repairs – FHWA ER
4. Hopper Ave Corridor Fire Recovery Improvements - PGE

Construction

1. Backup Generators – Water and Wastewater Facilities - HMGP
2. 6 Fire Damaged Parks Recovery – FEMA PA
3. Fire Damaged Roadway Landscaping Repair – FEMA PA



Fire Station 5 Resiliency and Relocation

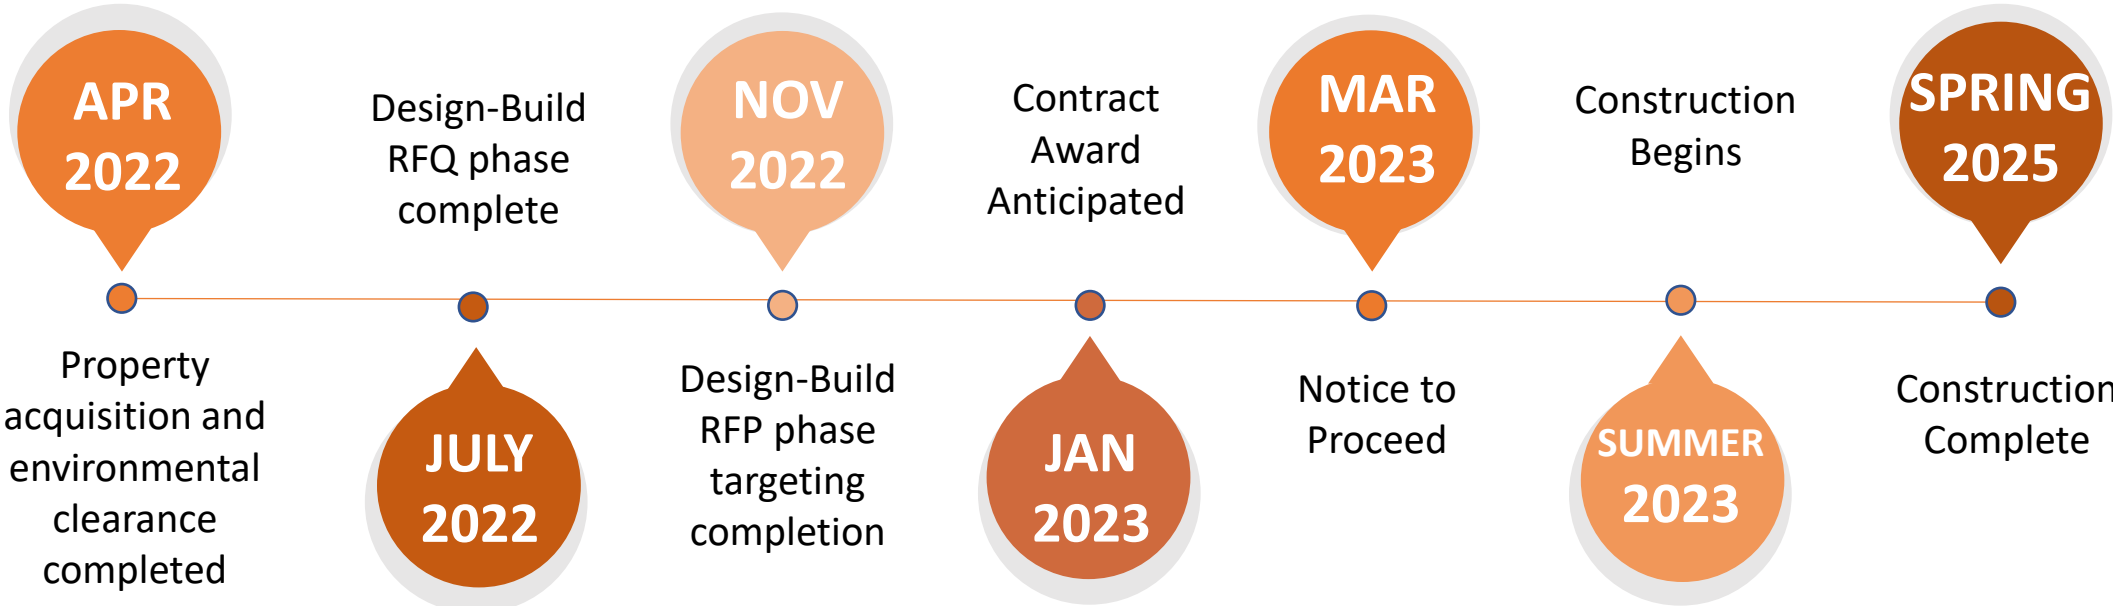

Fire Damaged Roadway Resiliency Improvements

- Resurface 36 miles of residential streets impacted by the debris removal mission
- Grant funding clearance: Summer 2022
 - Approx \$13.5M in CDBG-DR/INF
- Design build RFP: Summer 2022
- Contract award: Fall 2022
- Construction: Spring 2023 – Spring 2024



2017 Fire Damaged Roadway Repairs - FHWA

- Address roadway damages on:
 - Fountaingrove Parkway
 - Hopper Ave
 - Bicentennial Way
- Funded through FHWA Emergency Response program
 - \$4.75M Project
 - ~60% Federal match
- Caltrans approval to proceed with construction anticipated October 2022
- Award Project January 2023
- Construction Complete May 2023



Hopper Ave Corridor Fire Recovery Improvements

- Restore Hopper Ave between Hwy 101 S on ramp and Coffey Lane
- Project funded by PGE Settlement Funds
- July 2022: Public Engagement and Preliminary Design contract awarded
- September 2022: 1st Community scoping meeting
- Winter 2023 – Summer 2024: Design/Build Delivery
- Summer 2024: Project Complete



Backup Generators – Water and Wastewater Facilities

- Replace Backup Generators at water and wastewater facilities to ensure a more reliable fuel option
- Project Funding: FEMA HMGP
- Contract award: August 2022
- Construction: Fall 2022 – Fall 2023




Fire Damaged Roadway Landscaping Repair

- Replace roadside and median landscaping, irrigation and associated electrical services along Fountaingrove Parkway and in Coffey Park
- Funded by FEMA Public Assistance and PGE Settlement Funds
- Construction schedule: August 2022 – August 2023



Six Fire Damaged Parks – Recovery

- Restoration of:
 - Fir Ridge Park
 - Francis Nielsen Park
 - Nagasawa Park
 - Rincon Ridge Park
 - Rincon Ridge Open Space
 - Parker Hill Open Space
- Funded by FEMA Public Assistance and PGE Settlement Funds
- Construction began June 2022
- Completion in January 2023

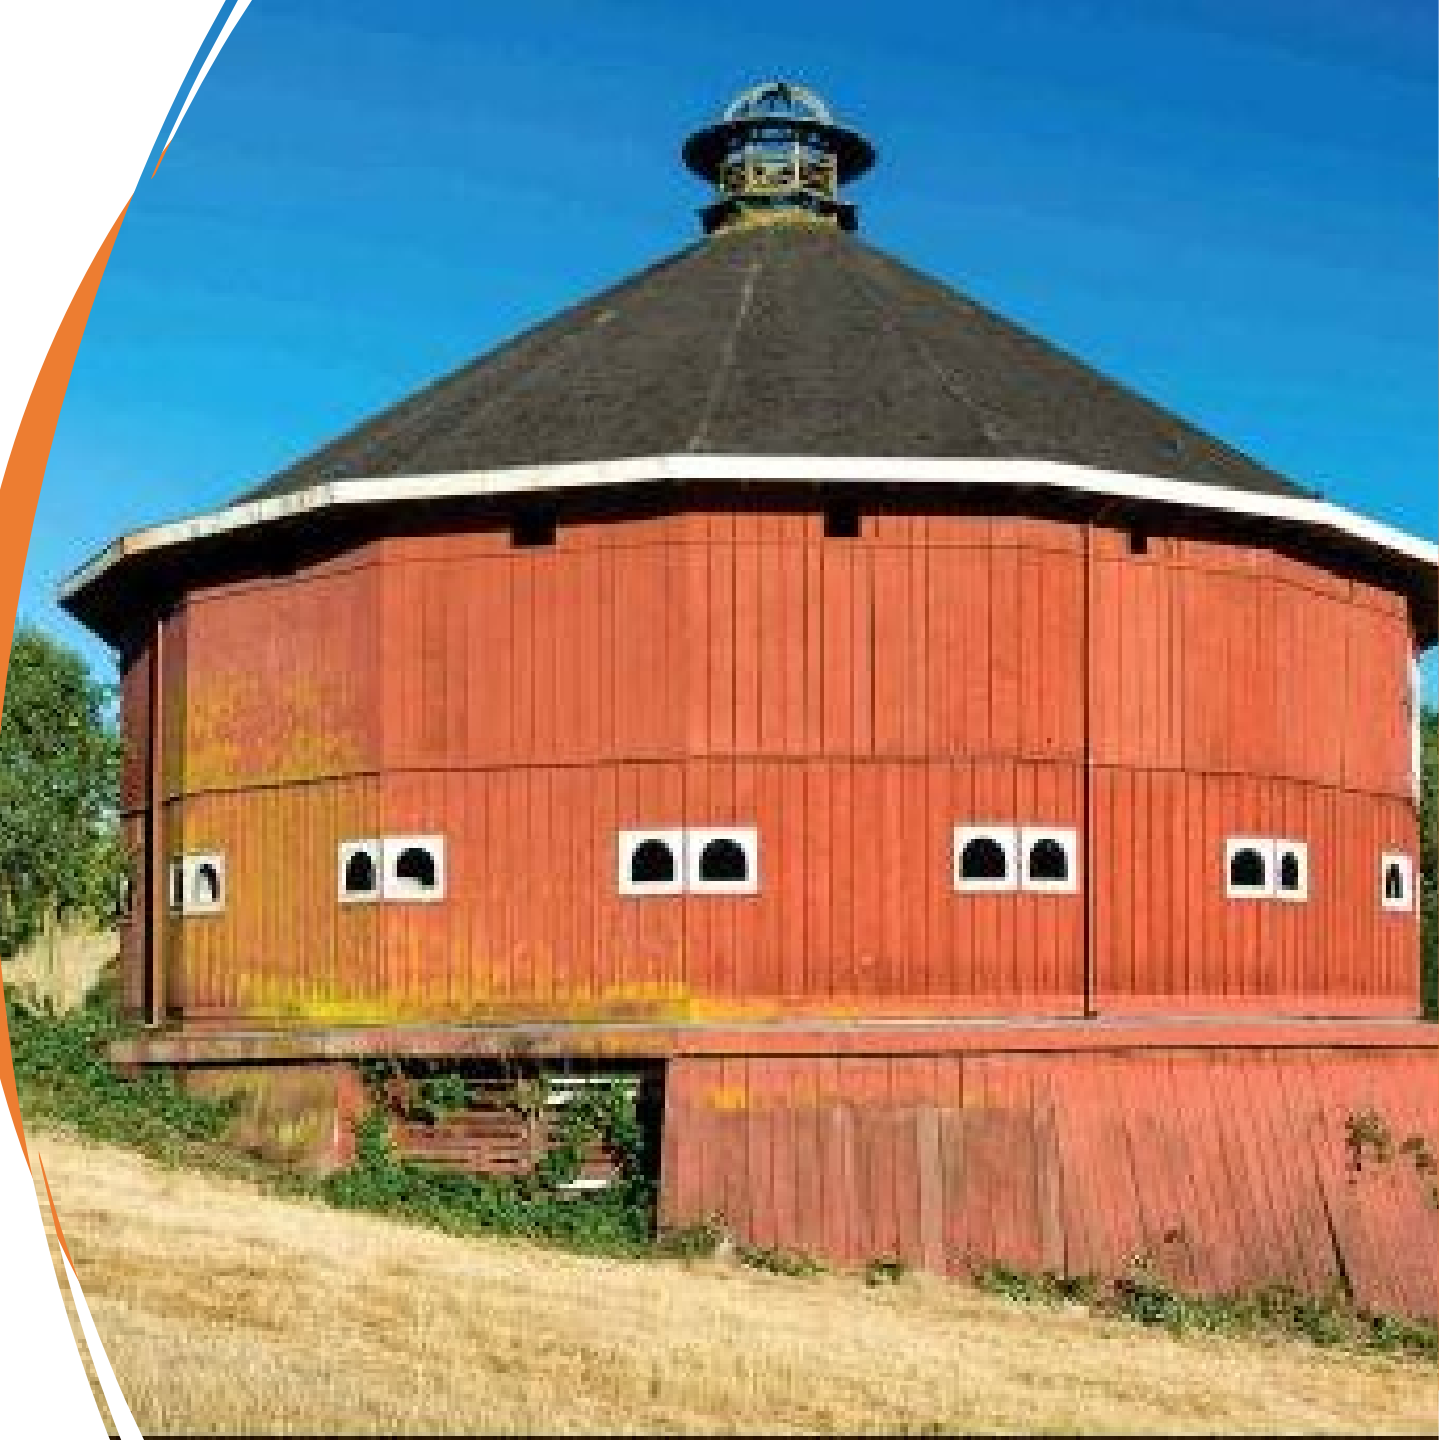

Financial Update

- Project Funding

FEMA – PA

- \$32.5M obligated
- \$17.8M reimbursed

FEMA – HMGP

- \$8.8M obligated
- \$2.1M reimbursed

Community Development Block Grant

- \$33M awarded (obligation pending)

FHWA - ER

- \$4.75M awarded (obligation pending)

PGE Settlement Funds

- \$20M dedicated by Council

- Project Closeout

- 8 Projects in closeout with FEMA



Questions?
